Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

PERT CHART

In-House Action Required For Stereo Comparator Delivery

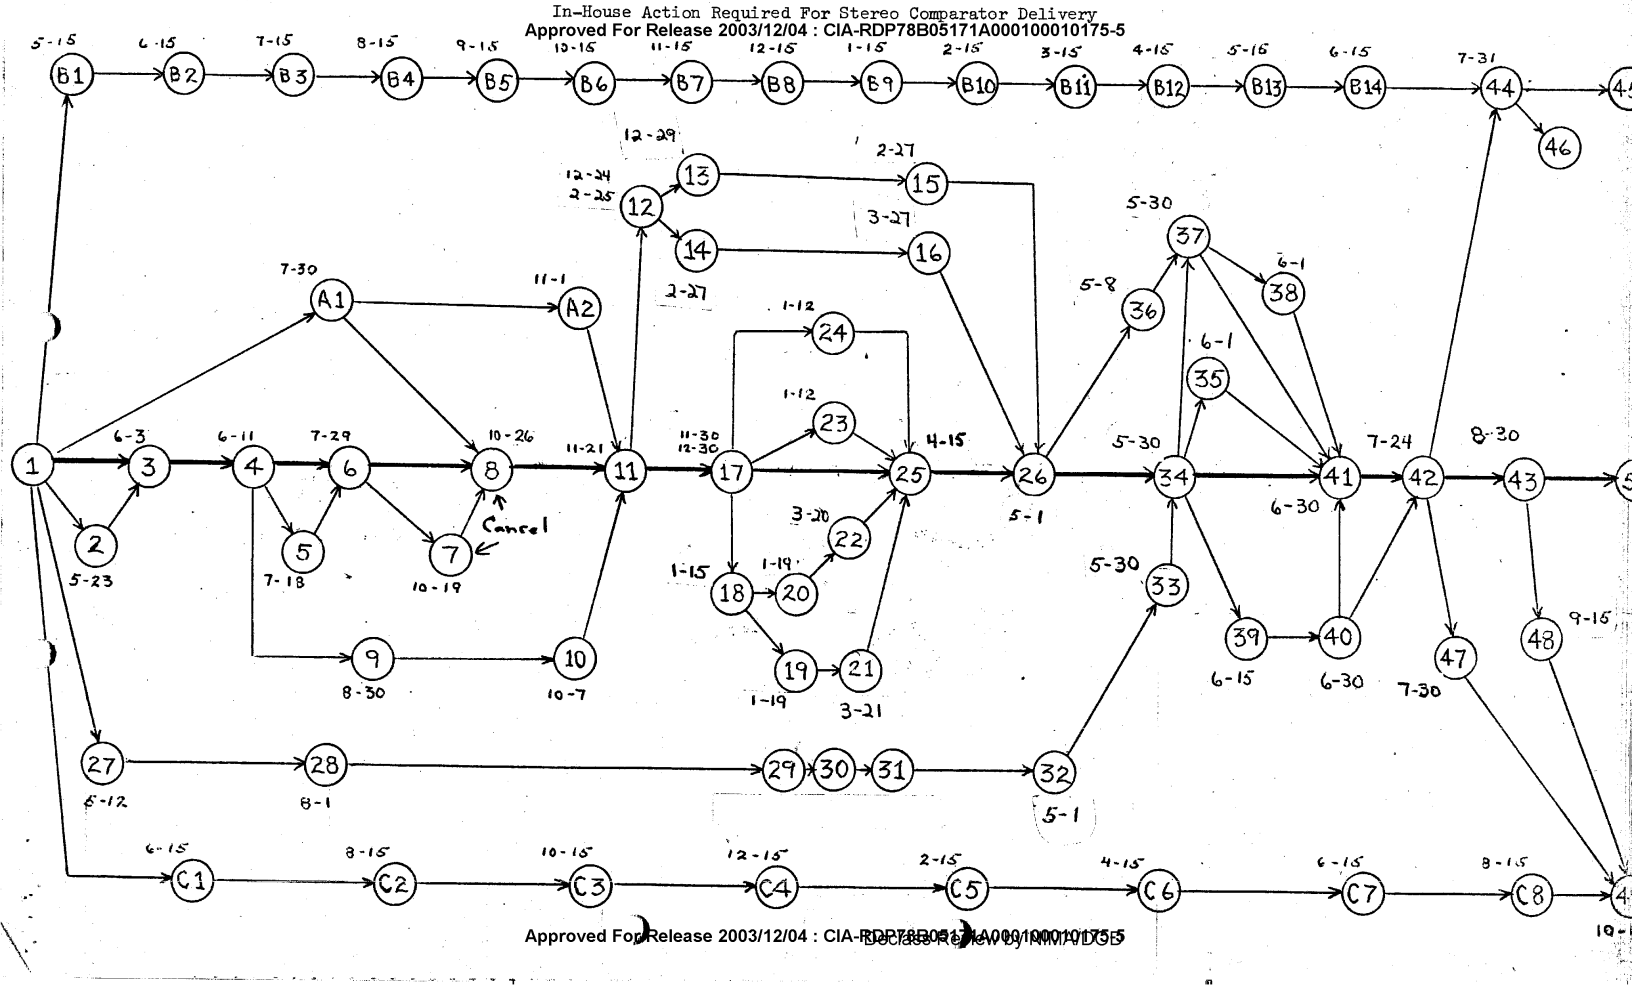

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5
Declass Review by NIMA/DXD

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

Revised 11-25-69

	EVENT	DESCRIPTION	
	1	Stereo Comparator Fabrication at [ ]	STAT
	2	IEG/PHD Provide Coordinate Test Data	
STAT	3	Digital Input Tests at [ ]	
STAT	4	[ ] Evaluate Digital Test Results Submit Spare Parts List to TSSG/ESD	
	5	IEG/PHD Provide Additional Test Data	
STAT	6	Computer Driven Tests at [ ]	
STAT	7	PSG/AID test [ ] Data Output for Compatibility	
	8	PSG/AID report results to [ ]	STAT
	9	TSSG/ESD review and revise Spare Parts List	
STAT	10	TSSG/ESD contract with [ ] for the revised Spare Parts List	
	11	Final Assembly of Subsystem (less optics) by [ ]	STAT
STAT	12	[ ] submit draft of Operating and Maintenance Manuals to TSSG/DED	
	13	IEG/PHD review and revise Operating Instruction Manual	
	14	TSSG/ESD review and revise Maintenance Manual	
	15	IEG/PHD approve Operating Instruction Manual	
	16	TSSG/ESD approve Maintenance Manual	
STAT	17	[ ] start final assembly at [ ]	STAT
	18	[ ] submit draft of Test Plan to TSSG/DED	
	19	IEG/PHD review Operational Test Plan	
	20	TSSG/ESD review and revise Test Plan	
	21	IEG/PHD approve Operational Test Plan	
	22	TSSG/ESD approve Test Plan	
	23	IEG/PHD provide representative imagery for pre-acceptance test	
	24	TSSG/ESD provide test targets and equipment	STAT
	25	System completely checked out and ready for pre-acceptance test at [ ]	
	26	Pre-acceptance test completed	STAT
	27	Final design of Clean Room reviewed and approved by [ ] Logistics [ ]	STAT
STAT	28	Site Preparation for [ ] Clean Room started	
	29	Clean Room site completed	
STAT	30	Logistics checkout [ ] Clean Room	
STAT	31	[ ] crew install cable trays, heavy wiring, etc. in [ ] Clean Room	STAT STAT
	32	Clean Room and Black Box checkout based on operation of instrument at [ ]	
	33	Logistics provide GSA moving crew	
STAT	34	[ ] starts installing the instrument in [ ] Clean Room	STAT

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

EVENT	DESCRIPTION
35	On-the-job Maintenance Training as instrument is installed
STAT 36	[redacted] submit draft of Programming Manual to PHD
37	[redacted] train IEG/PHD in instrument operation
38	IEG/PHD to provide operational imagery for acceptance tests
39	PSG/AID to have stereo and mono on-line programs ready to go
40	PSG/AID to make maximum on-line time available from 30 June 30 to 24 July 1969 to checkout and run acceptance tests on the instrument
41	Installation complete and acceptance tests start
STAT 42	NPIC-[redacted] acceptance tests complete
43	Final Acceptance Test by IEG/PHD and TSSG/ESD to be completed by 8 30
STAT 44	[redacted] submit final documentation to TSSG/DED
45	As built drawings completed
STAT 46	[redacted] submit all reports, drawings, ray traces, subcontractor reports, etc.
STAT 47	NPIC - Contracts pay [redacted] remaining progress payments 7 1/3% on each of following dates: 30, 60, 90 days after installation
48	Final Report on acceptance tests from IEG/PHD and TSSG/ESD to TSSG/DED
49	Incentive Fee Awarded and contract completed
50	Operational Tests and Training by IEG/PHD
A-1	FY-70 funding provided to complete project
A-2	Project out of funds if FY-70 funds is not provided
STAT B1-B14	[redacted] submits monthly and technical reports to TSSG/DED. Copies provided to IEG/PHD, TSSG/ESD and Logistics
C1-C8	TSSG/DED submits contract inspection reports to Contracts Administration

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

IEG/PHD	TSSG/ESD T&E//Maint.		LOGISTICS	PSG/AID	TSSG/DED	NPIC/PPBS MANAGEMENT
2, 3, 4, 5,	11	4, 9	27, 28, 29, 30,	7, 8, 39,	3, 4, 6, 11,	A-1
6, 13, 15, 19,	20	10	31, 32, 33, 34,	40	12, 18, 25,	A-2
21, 23, 25,	22	14	41, 42, 43		26, 34, 41,	
26, 36, 37, 38,	24	16			42, 43, 44,	
41, 42, 43, 48	25	35			46, 48, 49	
	26	45				
	41					
	42					
	43					
	48					

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

UNCLASSIFIED | CONFIDENTIAL | SECRET

CENTRAL INTELLIGENCE AGENCY

OFFICIAL ROUTING SLIP

TO	NAME AND ADDRESS	DATE	INITIALS
1	Deputy Chief, RED		
2	Chief, RED		
3	[redacted] Caleen (project [illegible] file)		
4			
5	Caleen File		
6			

	ACTION		DIRECT REPLY		PREPARE REPLY
	APPROVAL		DISPATCH		RECOMMENDATION
	COMMENT		FILE		RETURN
	CONCURRENCE		INFORMATION		SIGNATURE

Remarks:

Still have use going to have [illegible] for the file?

To 3
Make a copy of this I'd like to forward it to [redacted]

STAT

FOLD HERE TO RETURN TO SENDER

FROM: NAME, ADDRESS AND PHONE NO.	DATE

UNCLASSIFIED | CONFIDENTIAL | SECRET

Approved For Release 2003/12/04 : CIA-RDP78B05171A000100010175-5

(40)

FORM NO. 237 Use previous editions

U.S. GOVERNMENT PRINTING OFFICE : 1961 O—587282
